Sprint 3 Plan

Vitae | v.1 | Feb 11 – Feb 24, 2026 | Last Modified: 2026-02-24 | Revision #1

Goals

Users should be able to make edits without affecting their canon item. They should also be able to visualize their version history and group different resume versions into separate categories.

User Stories + Tasks

1. Override (3 points): As a user, I can override a canon or resume item's content for a specific resume without changing the original so that I can tailor it for different audiences. Berat Ercevik
    - 1.1. Modify API endpoint: PUT /working-state (2 hours) Berat Ercevik
    - 1.2. Add edit button to display an edit modal for each career history item on resume preview (0.5 hours) Berat Ercevik
    - 1.3. Implement edit functionality, similar to when entering in canon fields (2 hours) Berat Ercevik
    - 1.4. Implement data validation (non-empty input, matching canon forms) (1 hour) Berat Ercevik
    - 1.5. Show successful edit confirmation in UI (1 hour) Berat Ercevik
    - 1.6. Write unit tests for edit resume logic (2 hours) Berat Ercevik
    - 1.7. Write integration and/or unit test(s)/manual tests for full edit flow (2 hours) Berat Ercevik

Total hours for User Story 1: 10.5 hours

---

2. Regroup (4 points): As a user, I am able to save and group my versions as a list in a parent directory and perform operations on them. Alex Lio
    - 2.1. Be able to branch off of resumes and have the versions list be separated. Alex Lio (4 hours)
    - 2.2. Modify tables so that versions are grouped by a parent directory Alex Lio (1 hour)
    - 2.3. create and modify endpoint so that user can save to a chosen parent directory Alex Lio (3 hours)

Total hours for User Story 2: 8 hours

---

3. Visualize (4 points): As a user, I would like to be able to visualize my career history Omer Boztepe

3.1 Design git-tree style visualization UI for version history (2 hours) Omer Boztepe
3.2 Fetch and format version data from GET /versions endpoint (1 hour) Omer Boztepe
3.3 Implement timeline component showing version names and creation dates (3 hours) Omer Boztepe
3.4 Add visual tree structure with branches (1 hour) Omer Boztepe
3.5 Handle empty state (no versions) (1 hour) Omer Boztepe
3.6 Write unit tests for timeline data formatting (1 hour) Omer Boztepe
3.7 Write integration and/or unit test(s)/manual tests for visualization rendering (1 hour) Omer Boztepe

Total hours for User Story 2: 10 hours

---

4. Labelling Version History (1 point): As a user, I would like to be able to see which version I'm currently on and see it while previewing the resume. Berat Ercevik
   4.1. Integrate label UI on the resume preview page (1 hour) Berat Ercevik
   4.2. Extract version metadata on the resume preview page without adding more API calls Berat Ercevik (1 hour)
   4.3. Write unit tests to verify the correct version metadata for a particular version (2 hours) Berat Ercevik

---

5. PDF Export (2 points): As a user, I can download a PDF of my resume so that I can upload it to job sites. Njeri Gachoka
   5.1. Add PDF download API route (1 hour) Njeri Gachoka
   5.2. Add download button in frontend (1 hour) Njeri Gachoka
   5.3. Connect download button to API route (2 hours) Njeri Gachoka

Total hours for User Story 2: 4 hours

---

6. View Templates (4 points): As a user, I can view multiple preset templates to see which ones would best fit the role I'm applying to. Njeri Gachoka
   6.1. Make 4 more Typst templates (4 hours) Njeri Gachoka
   6.2. Make a button to select different templates with template preview (2 hours) Keith Tran

Total hours for User Story 2: 6 hours

---

7. Use Templates (2 points): As a user, I can use a template for my resume so that I can match the resume's visual style to different industries or preferences. Keith Tran
   7.1. Somewhere in the resume preview have a button to view and apply a resume template for a working state (1 hour) Keith Tran
   7.2. Have an additional field to store the template of the resume used (2 hours) Keith Tran

---

Role Assignments:

Njeri Gachoka - Developer, Product Owner
Keith Tran - Developer
Alex Lio - Developer, Scrum Master
Berat Ercevik - Developer
Omer Boztepe - Developer

Initial Task Assignments:

See user story and task listings above

Initial Burnup Chart:

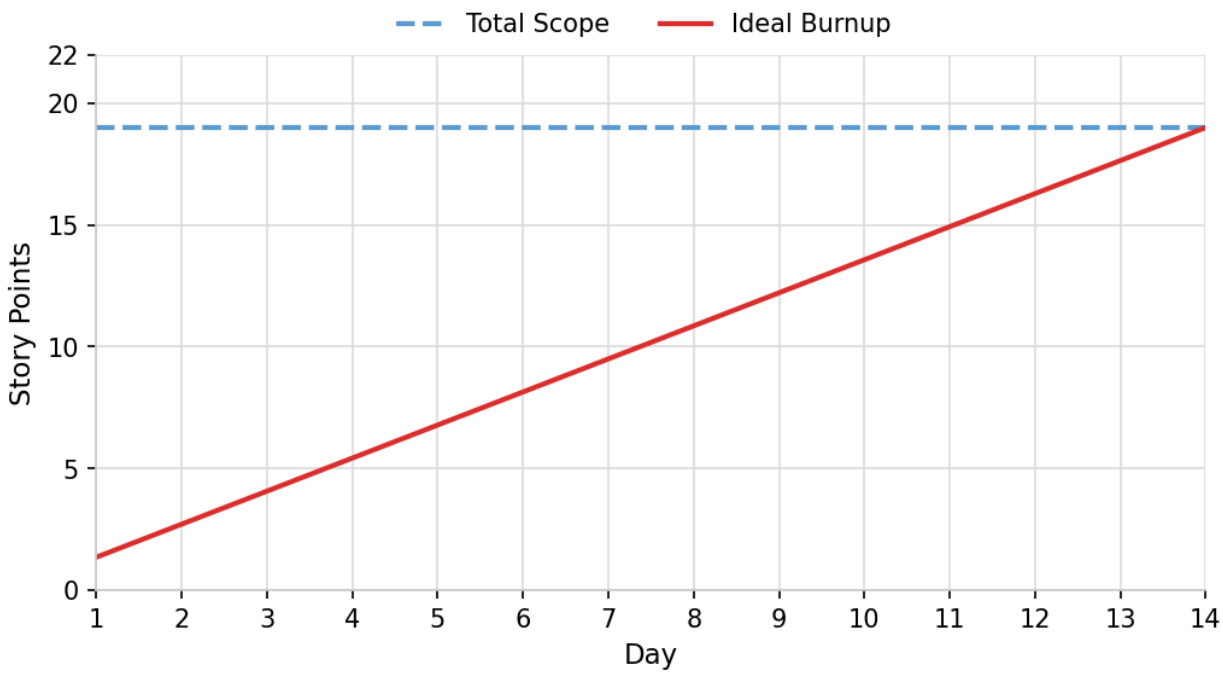

Final Burnup Chart:

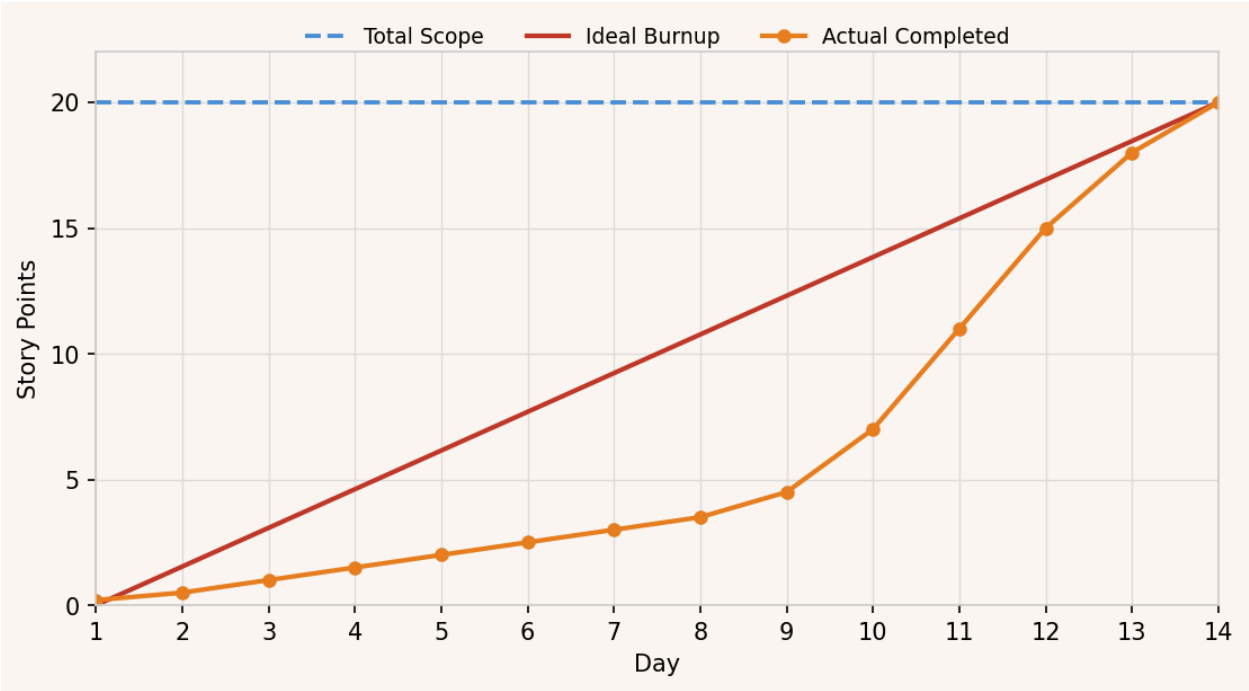

Scrum Board

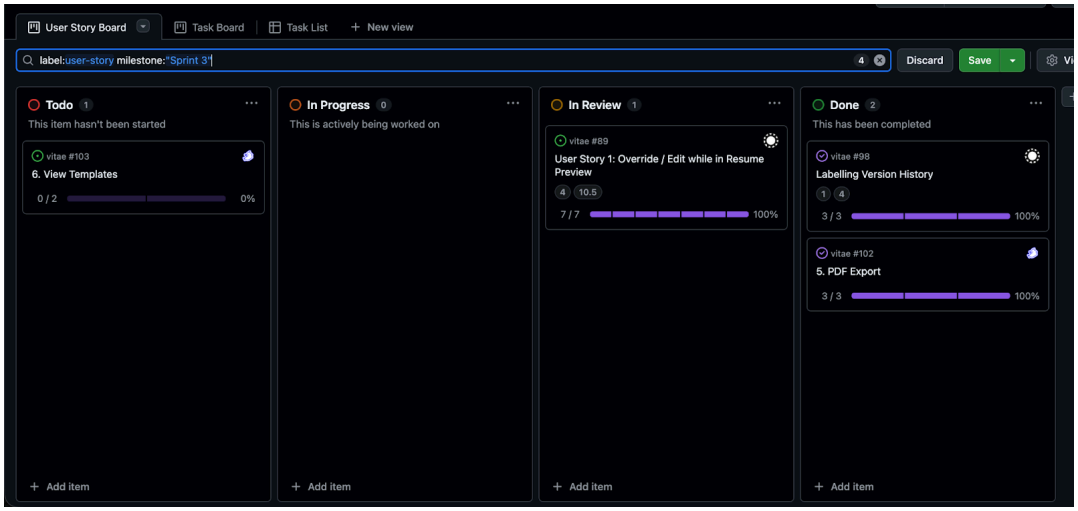

Scrum Times:

Friday 12:00pm - 1:00pm (TA meeting with Michelle Quach)
Friday 1:00pm - 1:15pm
Tuesday 10:00am - 10:15am
Sunday 10:00am - 10:15am
Monday 7:00pm - 9:00pm (Optional) general work-together hours
