Sprint 4 Plan

Vitae | v.1 | Feb 24 – Mar 10, 2026 | Last Modified: 2026-03-10

Goals

Users should be able to quickly adapt their experiences for different audiences with intelligent suggestions.

User Stories + Task Assignments

1. Diff check (3 points): As a user, I can compare two versions of my resume side-by-side so that I can see what changed between resume submissions. Keith Tran

    1.1. Design diff view UI with side-by-side layout (2 hours) Keith Tran
    1.2. Add version selector dropdowns (pick two versions to compare) (1 hour) Keith Tran
    1.3. Implement JSON diff logic for resume snapshots (2 hours) Keith Tran
    1.4. Highlight added/removed/changed items in UI (2 hours) Keith Tran
    1.5. Handle edge cases (1 hour) Keith Tran

Total hours for User Story 1: 8 hours

---

2. Quick build (3 points): As a user, I can paste a job description and see which canon items are most relevant so that I can quickly build a targeted resume. Berat Ercevik

    2.1. Design job description input UI (2 hours) Berat Ercevik
    2.2. Configure Gemini LLM API key and endpoint (1 hour) Berat Ercevik
    2.3. Design LLM prompt (1 hour) Berat Ercevik
    2.4. Implement logic to call API and rerank and select canon items (2 hours) Berat Ercevik
    2.5. Create endpoint to embed job description and compute reorderings and selections (3 hours) Berat Ercevik
    2.6. Display relevance-ranked canon items in UI automatically (2 hours) Berat Ercevik
    2.7. Write manual testing for similarity rerank(2 hours) Berat Ercevik

Total hours for User Story 2: 13 hours

---

3. AI tailoring (4 points): As a user, I can get AI-suggested revisions of my experiences for a specific role so that I can tailor my language efficiently.

    3.1. Design UI for requesting AI revision (button per canon item) (2 hours) Omer Boztepe
    3.2. Create endpoint to generate tailored version of item (3 hours) Omer Boztepe
    3.3. Write prompt template for reframing experience (2 hours) Omer Boztepe
    3.4. Display AI suggestion alongside original (2 hours) Omer Boztepe
    3.5. Add accept/reject actions for suggestion (1 hour) Omer Boztepe
    3.6. Save accepted revision as override (1 hour) Omer Boztepe
    3.7. Write manual tests for prompt generation (1 hour) Omer Boztepe

Total hours for User Story 3: 12 hours

---

4. View Tailoring Options (6 points): As a user, I want to see the space of tweaks that can reasonably be made to my resume item so that I don't have to reprompt an LLM over and over with ways to tweak it.

    4.1. Define tailoring axes (industry, tone, technical depth, length, etc.) (2 hours) Njeri Gachoka
    4.2. Design form in the UI for tweaks (3 hours) Njeri Gachoka
    4.3. Map axis values to prompt parameters (2 hours) Njeri Gachoka
    4.4. Create an endpoint that accepts axis values and generates tailored text (3 hours) Njeri Gachoka
    4.5. Write prompt template with parametrized tone/industry/etc (2 hours) Njeri Gachoka
    4.6. Display generated text (2 hours) Njeri Gachoka
    4.7. Cache recent axis combinations to avoid redundant LLM calls (2 hours) Njeri Gachoka
    4.8. Write unit/manual tests for axis-to-prompt mapping (2 hours) Njeri Gachoka

Total hours for User Story 4: 18 hours

---

5. Archive Bin (4 points): As a user, I would like deleted career items to be recoverable from a "Recently Deleted" bin so I can restore them or view them in older resume snapshots.
    5.1. Design canon_archive table schema and write migration SQL (1 hour) Alex Lio

5.2. Modify DELETE /api/canon to soft-delete (INSERT into archive, then DELETE from live table) (1.5 hours) Alex Lio
5.3. Build GET /POST /DELETE /api/archive route with 30-day lazy expiry (3 hours) Alex Lio
5.4. Update POST /api/versions/[id]/restore to resolve and return archived items referenced by snapshot (1.5 hours) Alex Lio
5.5. Add ArchivedCanonItem type and Zod validation schema to shared layer (0.5 hours) Alex Lio
5.6. Create api client functions (list, restore, permanently delete) (1 hour) Alex Lio
5.7. Update useVersion to save archived items to sessionStorage post-restore (1 hour) Alex Lio
5.8. Update useResumeBuilder to merge archived items into preview item pool (1.5 hours) Alex Lio
5.9. Update ResumeBuilderPage to read archived items from sessionStorage on mount (1 hour) Alex Lio
5.10. Build ArchiveBin collapsible UI component with Restore / Delete Forever actions (2 hours) Alex Lio
5.11. Wire ArchiveBin into home page with canon list refresh callback (0.5 hours) Alex Lio
5.12. Write unit/manual tests for archive client API and sessionStorage bridge (2 hours) Alex Lio

Total hours for Archive Bin: 17 hours

Role Assignments

Njeri Gachoka : Developer, Product Owner
Keith Tran : Developer
Alex Lio : Developer
Berat Ercevik : Developer
Omer Boztepe : Developer, Scrum Master

Initial Task Assignments:

See user story and task listings above

Initial Burnup Chart

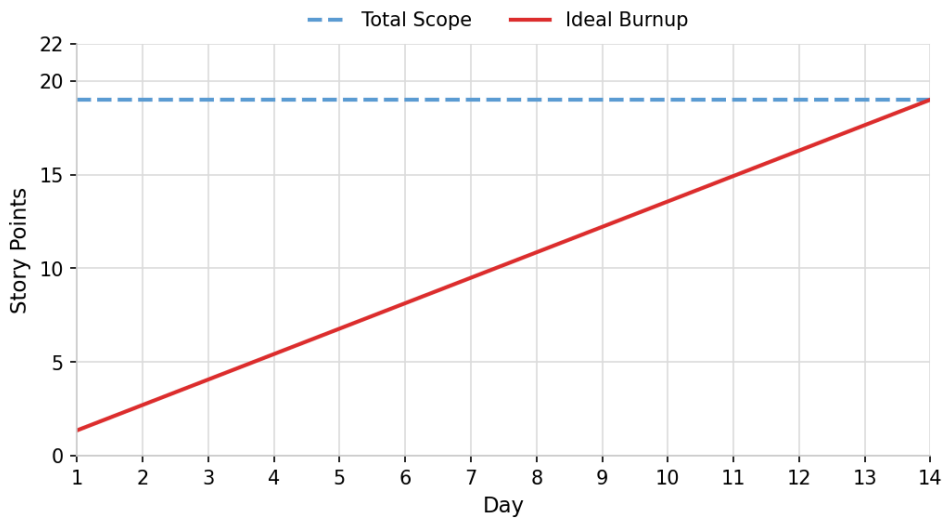

Final Burnup Chart

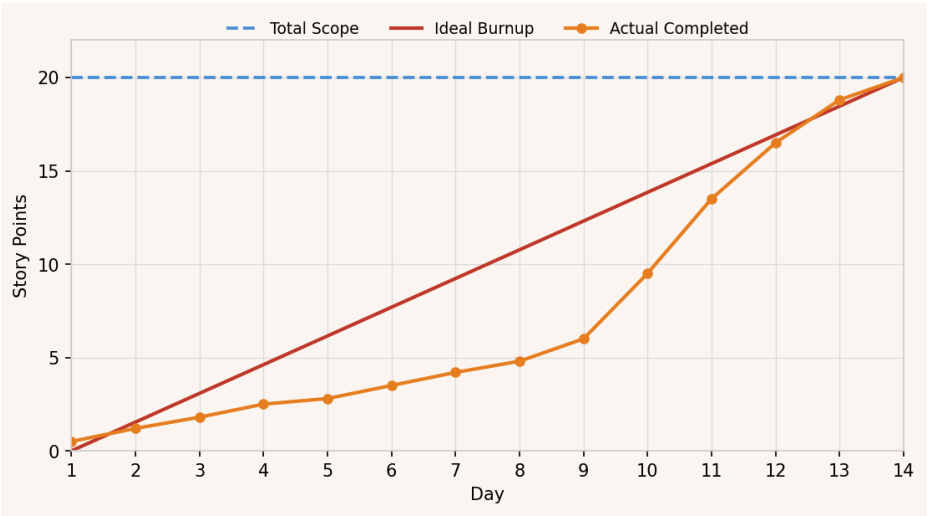

Scrum Board

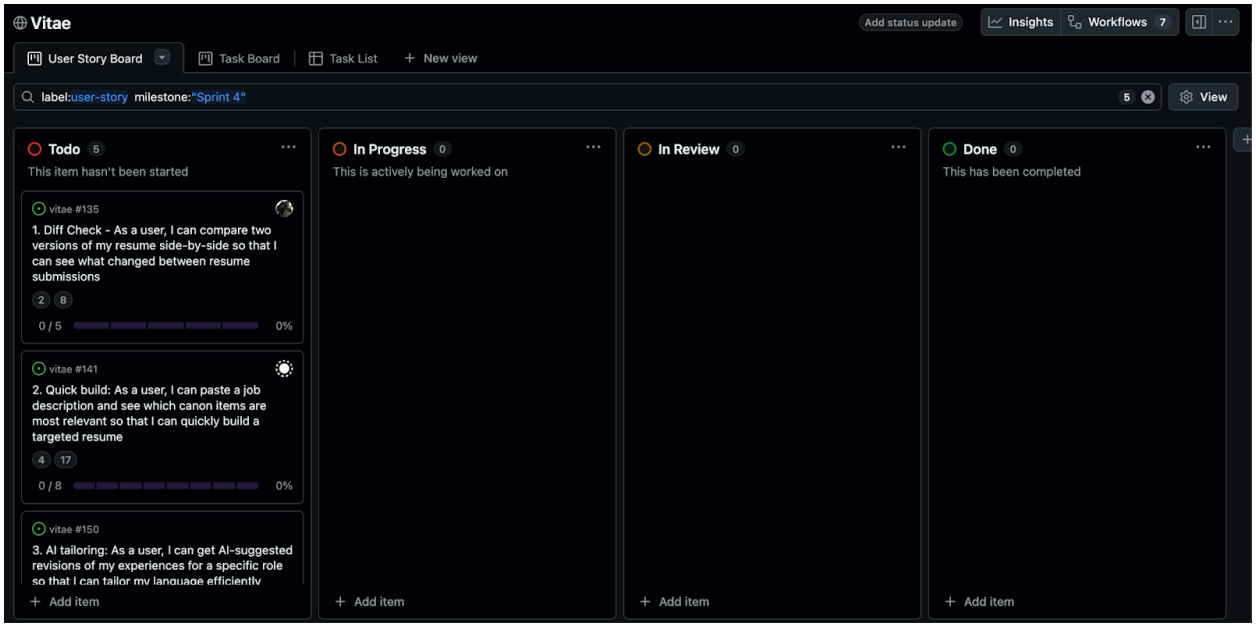

Scrum Times:

Friday 12:00pm - 1:00pm (TA meeting with Michelle Quach)
Friday 1:00pm - 1:15pm
Tuesday 10:00am - 10:15am
Sunday 10:00am - 10:15am
Monday 7:00pm - 9:00pm (Optional) general work-together hours
